



CERTIFICATE OF QUALITY

EverFast™ Type HE Cement

NZS 3122:2009



Our
NZ made
cement is
genuine
NZ grade
cement.

Issued to: *Technical Sales Manager*

Test Report No: **19#291**

info@goldenbay.co.nz

Code	Week Ending	Specific Surface Area	Normal Consistency	Initial Set	Final Set	Soundness	Compressive Strength								Free Lime	Sodium Equivalent (NaEq)	Sulphur Trioxide (SO3)	
							ISO-CEN				Concrete							
							1 Day	3 days	7 days	28 days	Slump	1 Day	3 days	7 days				28 days
Mean		510	32.8	121	3:06	1	23.8	41.5	50.2	66.0	85.8	17.3	35.3	42.7	52.3	1.9	0.53	2.4
Standard Deviation		15	1.1	12	0:15	0.4	1.0	1.0	1.2	0.8	4.8	1.3	1.7	1.6	1.7	0.3	0.02	0.0
Min		490	28.2	105	2:45	0	22.3	39.3	48.3	64.7	75.0	14.6	32.7	39.6	49.0	1.4	0.49	2.3
Max		545	34.2	135	3:30	2	26.0	44.2	52.8	67.8	90.0	19.8	38.9	45.8	55.1	2.4	0.56	2.5
NZS 3122:2009 Requirements				45 min	6:00 max	5 max		25.0 min	40.0 min								0.6 max	3.5 max
Units		m2/kg	%	minutes	hrs:mins	mm	Mpa	MPa	MPa	MPa	mm	Mpa	MPa	MPa	MPa	%	%	%
191213-604-HE	13/12/19	500	33.0	120	2:45	1	22.3	41.1			85	18.3	32.9			1.6	0.53	2.4
191127-837-HE	27/11/19	520	32.9	105	3:00	1	23.4	41.6	50.1		80	19.5	34.6	43.3		2.2	0.55	2.4
191115-185-HE	15/11/19	495	32.8	135	3:15	2	26.0	42.4	52.8	66.9	90	16.3	33.2	40.1	49.0	1.6	0.53	2.4
191024-351-HE	24/10/19	505	33.0	120	2:45	1	24.0	42.4	50.0	67.8	85	17.3	34.1	42.0	49.9	2.4	0.53	2.4
191017-573-HE	17/10/19	490	33.0	120	3:00	1	24.2	41.4	49.1	65.1	85	16.5	32.9	41.9	52.4	1.9	0.51	2.4
191001-054-HE	01/10/19	520	32.7	105	2:45	2	24.6	41.8	48.7	65.2	90	17.9	35.7	42.1	53.1	2.0	0.53	2.5
190920-350-HE	20/09/19	520	32.6	105	3:00	1	22.8	40.4	51.0	65.1	85	17.0	35.6	41.3	55.0	1.8	0.52	2.4
190908-041-HE	08/09/19	515	32.7	105	2:45	1	23.5	42.3	49.0	65.4						1.6	0.52	2.4
190830-237-HE	30/08/19	520	32.7	105	2:45	1	24.4	40.3	49.0	64.8	90	19.6	35.7	42.6	53.6	1.7	0.50	2.5
190810-294-HE	10/08/19	510	32.6	120	3:00	0	24.4	40.8	50.0	65.2	90	17.4	36.1	45.5	55.1	1.5	0.49	2.4
190727-356-HE	27/07/19	490	28.2	120	3:15	1	23.0	39.3	49.6	66.0	90	15.9	34.4	43.7	52.5	1.4	0.52	2.3
190712-708-HE	12/07/19	525	33.0	105	3:30	1	25.7	42.7	50.9	66.2	90	17.6	38.9	44.5	51.8	2.2	0.53	2.4
190628-132-HE	28/06/19	495	31.6	120	2:45	1	25.7	44.2	51.3	66.5	90	17.5	36.5	42.2	51.1	2.2	0.56	2.4
190609-519-HE	09/06/19	490	31.6	120	3:15	1	23.2	39.9	48.3	65.6	80	19.0	36.2	43.9	51.7	1.9	0.52	2.3
190526-813-HE	26/05/19	495	32.6	135	3:15	1	23.9	41.4	49.5	65.3	85	19.1	36.6	44.1	52.5	2.1	0.54	2.3
190517-107-HE	17/05/19	495	33.0	135	3:15	1	23.3	40.6	51.6	66.6	80	16.4	35.0	42.8	52.7	1.7	0.54	2.4
190415-644-HE	15/04/19	505	33.0	120	3:15	1	25.0	41.4	50.9	66.2	90	14.6	32.7	41.7	50.8	2.1	0.56	2.4
190331-978-HE	31/03/19	500	33.1	135	3:30	1	22.7	42.1	51.6	65.2	90	16.5	35.0	42.1	54.7	2.2	0.54	2.4
190316-142-HE	16/03/19	500	33.0	135	3:30	1	24.4	42.3	50.9	64.7	90	16.5	35.0	42.3	50.2	1.7	0.56	2.5
190217-668-HE	17/02/19	510	33.2	135	3:30	1	23.8	41.7	48.8	66.7	90	15.7	34.3	41.5	51.5	1.9	0.55	2.4
190208-223-HE	08/02/19	525	33.8	120	3:15	1	23.1	42.3	50.5	66.6	80	17.2	37.4	42.1	52.8	1.7	0.51	2.4
190119-778-HE	19/01/19	535	33.6	105	3:15	1	23.8	41.3	52.1	66.2	75	19.8	37.3	45.5	51.3	1.7	0.49	2.4
190109-190-HE	09/01/19	515	33.3	135	3:15	1	23.1	41.4	50.9	67.0	90	16.8	33.3	39.6	54.2	2.1	0.52	2.4
181201-154-HE	01/12/18	520	34.1	120	3:00	2	23.3	41.5	48.8	66.1	80	16.7	38.4	45.8	53.9	1.5	0.53	2.4
181123-508-HE	23/11/18	545	34.2	135	3:00	1	22.4	41.0	50.7	67.3	80	17.1	35.1	42.2	50.8	1.6	0.54	2.3

The above samples were tested as received in accordance with the current terms of accreditation and methods stated in NZS 3122:2009 with the exception of:
 - Chemical Analysis to ASTM C114-18
 - Concrete Compressive Strength test results outside the scope of accreditation

This Report must not be reproduced except in full



Portland Works, Portland, Whangarei 0178

Jim White

Jim White
Quality System Co-ordinator

Date issued: 20/12/19

Page 1 of 3

-Sample retested
 # -No result available at time of certificate issue




**EverFast™
Type HE Cement**



Compressive Strength ISO-CEN Mortar

—x— 28 Days —■— 7 Days —◆— 3 Days —x— 1 Day

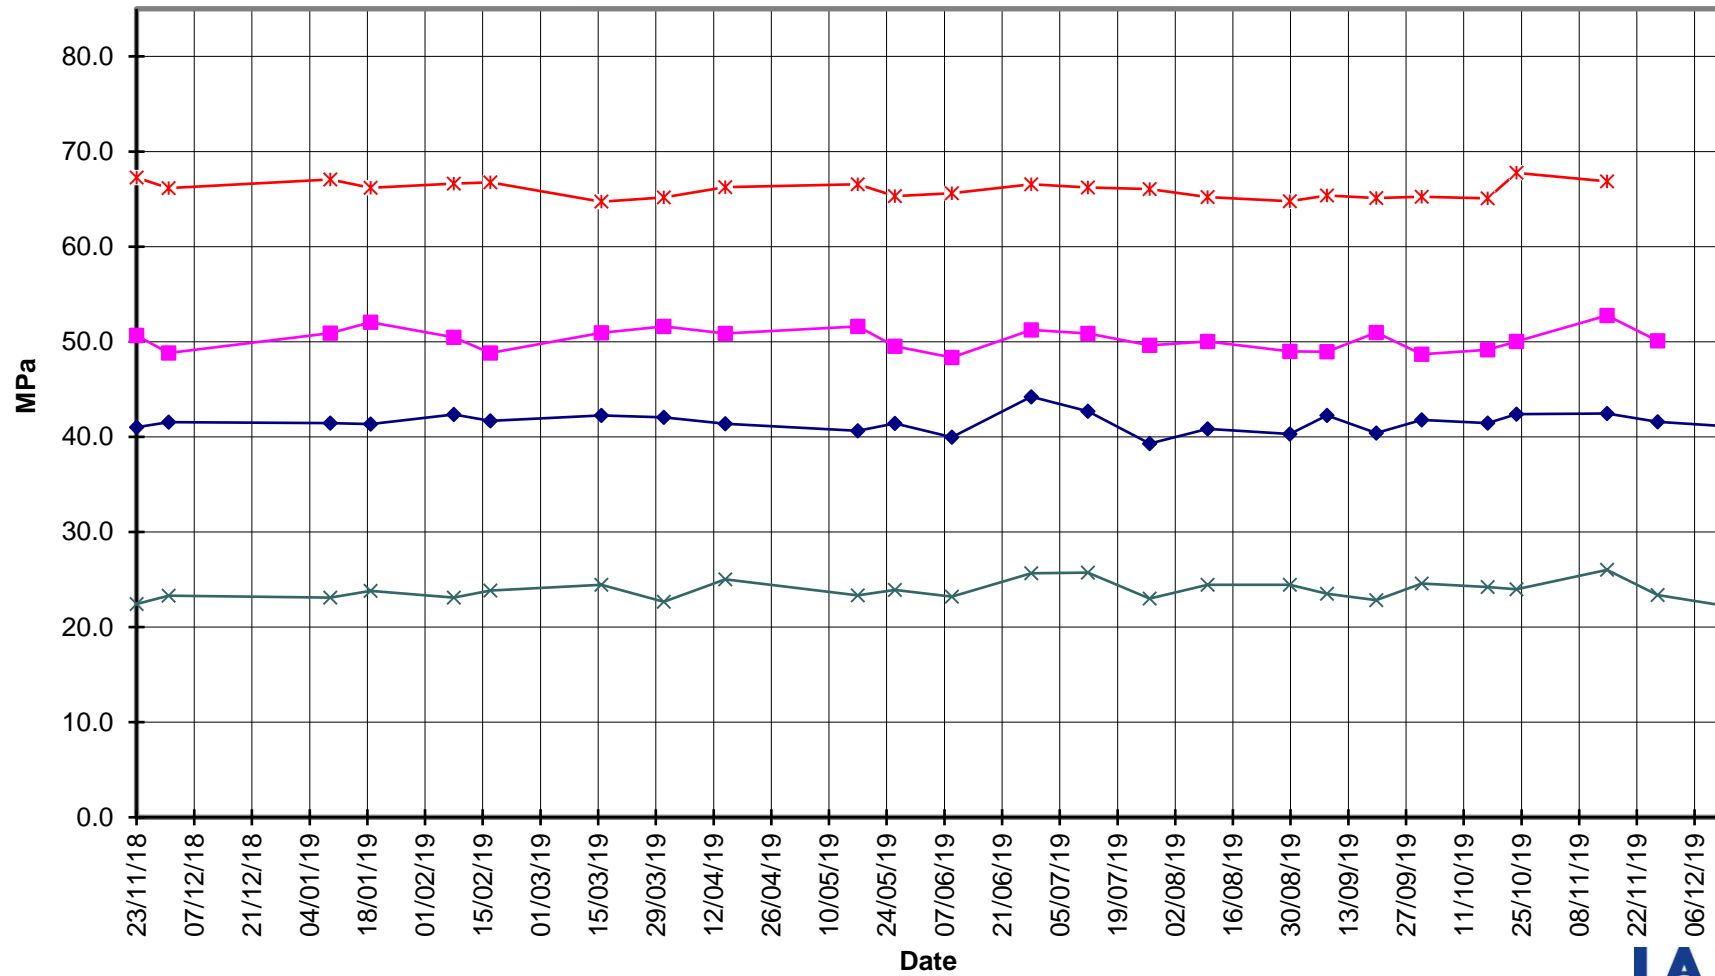



EverFast™ Type HE Cement



Compressive Strength Concrete

—x— 28 Days —■— 7 Days —◆— 3 Days —x— 1 Day —*— Slump

