



CERTIFICATE OF QUALITY

EverSure™ Type GP Cement

NZS3122:2009 (Bulk Despatch)



Our
NZ made
cement is
genuine
NZ grade
cement.

Issued to: National Sales Manager

Test Report No: 22#44

info@goldenbay.co.nz

Code	Week Ending / Voyage	Specific Surface Area	Normal Consistency	Initial Set	Final Set	Soundness	Compressive Strength							Free Lime	Sodium Equivalent (NaEq)	Sulphur Trioxide (SO3)
							ISOCEN			Concrete						
							3 days	7 days	28 days	Slump	3 days	7 days	28 days			
Mean		337	29.2	143	3:49	1	31.1	43.0	64.7	95	22.9	32.9	46.4	1.8	0.56	2.3
Standard Deviation		10	0.4	13	0:21	0	1.0	1.3	0.9	7	2.3	3.4	3.1	0.2	0.01	0.07
Min		320	28.6	120	3:15	0	28.7	39.7	63.4	80	20.2	26.5	43.2	1.4	0.54	2.2
Max		365	30.4	165	4:30	2	33.1	44.8	66.7	100	26.5	39.7	51.7	2.3	0.57	2.4
NZS 3122:2009 Requirements				45 min	6:00 max	5 max		35.0 min	45.0 min						0.6 max	3.5 max
Units		m2/kg	%	minutes	hrs:mins	mm	MPa	MPa	MPa	mm	MPa	MPa	MPa	%	%	%
220420-977-GP	20/04/22	365	28.8	165	4:15	1	31.1							2.0	0.56	2.2
220416-828-GP	16/04/22	360	28.8	165	4:00	1	30.6			100	20.2			1.9	0.56	2.2
220415-398-GP	15/04/22	340	29.1	150	4:30	0	32.0	44.5						2.2	0.55	2.2
220410-396-GP	10/04/22	330	29.1	165	4:30	0	29.8	39.7		100		29.2		1.9	0.56	2.2
220406-210-GP	06/04/22	320	29.2	135	3:30	2	31.0	43.8						1.8	0.55	2.2
220404-208-GP	04/04/22	320	29.0	150	3:45	1	28.7	40.8		100	22.0	31.6		1.6	0.55	2.2
220330-027-GP	30/03/22	340	29.3	135	3:45	1	33.1	43.9		100	20.4	32.1		2.1	0.56	2.2
220328-025-GP	28/03/22	340	29.3	150	3:45	1	30.3	40.7						2.2	0.56	2.2
220326-790-GP	26/03/22	345	29.0	150	3:30	1	30.3	42.6	64.8	100	21.2	30.9	44.6	1.8	0.57	2.3
220323-788-GP	23/03/22	335	29.0	150	3:30	2	31.9	43.0	64.8					2.1	0.56	2.2
220317-660-GP	17/03/22	335	28.9	150	3:45	2	30.4	43.6	64.9	90	25.6	33.8	44.8	1.9	0.56	2.2
220310-136-GP	10/03/22	340	30.0	150	4:15	1	32.4	44.4	64.2					2.3	0.57	2.3
220306-133-GP	06/03/22	330	29.3	150	4:15	1	30.6	41.8	63.9	80	24.3	35.9	43.7	2.1	0.57	2.3
220228-856-GP	28/02/22	350	29.0	150	3:30	1	29.8	43.1	64.5	90	25.6	39.7	46.3	1.6	0.57	2.3
220226-646-GP	26/02/22	345	29.1	135	3:30	2	31.3	43.3	64.1	100	22.4	30.8	44.4	1.4	0.56	2.4
220221-648-GP	21/02/22	335	29.0	135	3:30	1	31.5	44.8	64.6	100	21.9	31.2	43.6	1.6	0.57	2.2
220217-261-GP	17/02/22	330	29.6	135	4:15	2	31.4	41.8	65.8	90	26.5	36.3	51.7	1.5	0.56	2.3
220215-259-GP	15/02/22	335	29.2	135	4:15	1	31.8	43.3	66.5					1.5	0.57	2.2
220214-907-GP	10/02/22	340	30.4	120	3:45	1	32.7	44.4	66.7					1.7	0.55	2.4
220214-906-GP	08/02/22	335	29.0	120	3:30	1	32.0	44.1	64.9	100	20.2	31.5	47.8	1.8	0.54	2.4
220206-419-GP	06/02/22	340	29.2	135	3:45	1	31.8	43.4	63.4					1.6	0.54	2.4
220204-417-GP	04/02/22	335	29.1	150	3:45	1	30.7	43.1	63.6	80	25.6	34.6	49.4	1.6	0.56	2.4
220129-097-GP	29/01/22	330	29.1	135	3:45	1	30.6	42.9	64.7	100	20.7	26.5	43.2	1.8	0.55	2.4
220126-095-GP	26/01/22	325	29.1	135	3:30	1	30.8	43.4	64.1					1.6	0.56	2.3
220120-744-GP	20/01/22	335	28.6	120	3:15	2	30.3	43.1	64.8	90	24.3	36.0	50.8	2.1	*0.53	*2.3

The above samples were tested as received in accordance with the current terms of accreditation and methods stated in NZS 3122:2009 with the exception of:

Chemical composition to ASTM C114-18

- Concrete Compressive Strength test results outside the scope of accreditation

No result available at time of certificate issue
* Tested by SpectraChem Analyticsl - Verrum Group

This Report must not be reproduced except in full

Raki Harding
Quality Manager

Date issued: 4/29/2022



Portland Works, Portland, Whangarei 0178

Page 1 of 3




EverSure™ Type GP Cement



Compressive Strength ISO-CEN Mortar (Bulk Dispatch)

28 Days 7 Days 3 Days

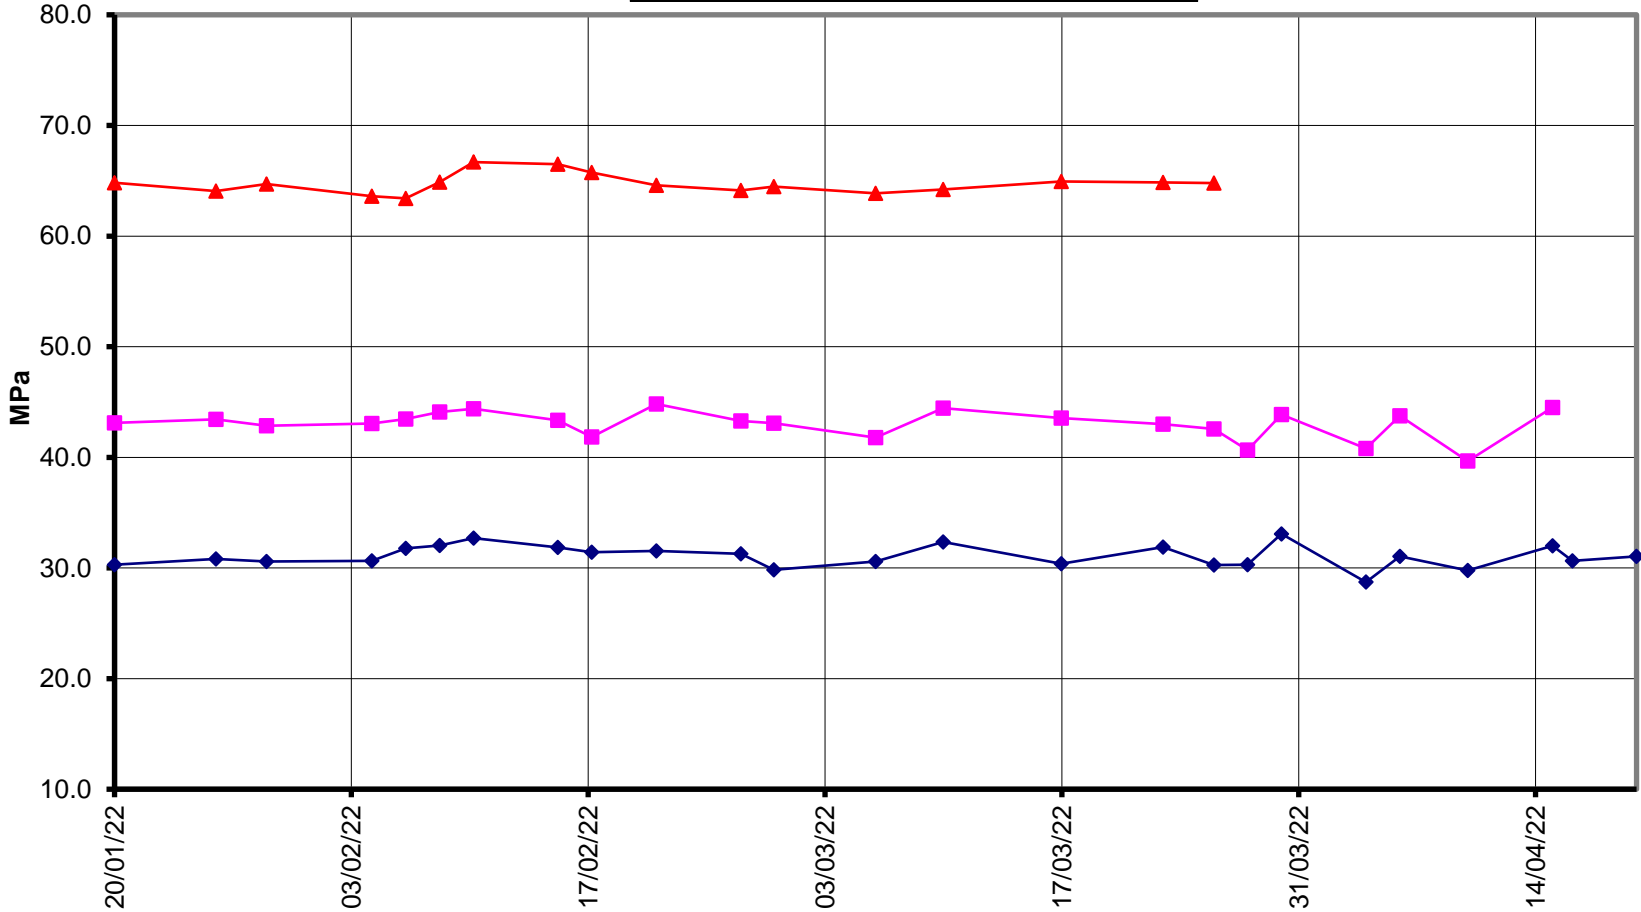

Date





EverSure™ Type GP Cement



Compressive Strength Concrete (Bulk Dispatch)

—x— 28 Days —■— 7 Days —◆— 3 Days —x— Slump

