



# CERTIFICATE OF QUALITY

## EverSure™ Type GP Cement

NZS3122:2009 (Bulk Despatch)



Our  
NZ made  
cement is  
**genuine**  
NZ grade  
cement.

Issued to: National Sales Manager

Test Report No: 22#65

info@goldenbay.co.nz

Code	Week Ending / Voyage	Specific Surface Area	Normal Consistencv	Initial Set	Final Set	Sound-ness	Compressive Strength							Free Lime	Sodium Equivalent (NaEq)	Sulphur Trioxide (SO3)
							ISOCEN			Concrete						
							3 days	7 days	28 days	Slump	3 days	7 days	28 days			
Mean		338	29.2	144	3:55	1	30.4	43.1	64.5	94	22.5	33.0	46.6	2.1	0.57	2.2
Standard Deviation		13	0.4	11	0:18	0	0.9	1.5	1.2	10	1.5	1.5	2.1	0.3	0.01	0.04
Min		320	28.6	120	3:30	0	28.8	39.6	62.4	70	20.1	30.3	42.5	1.7	0.54	2.1
Max		365	30.4	165	4:30	2	32.2	46.3	66.5	110	24.1	35.5	49.9	2.8	0.59	2.3
NZS 3122:2009 Requirements				45 min	6:00 max	5 max		35.0 min	45.0 min						0.6 max	3.5 max
Units		m2/kg	%	minutes	hrs:mins	mm	MPa	MPa	MPa	mm	MPa	MPa	MPa	%	%	%
220713-838-GP	13/07/22	345	29.2	135	3:30	0	30.1							1.9	0.58	2.3
220710-836-GP	10/07/22	345	28.8	150	4:30	1	31.6			100	20.7			1.8	0.58	2.2
220706-670-GP	06/07/22	325	29.2	135	3:45	1	31.1	43.8		90	23.5	35.5		2.0	0.58	2.2
220704-677-GP	04/07/22	320	29.2	135	3:30	1	30.4	43.8						1.8	0.56	2.2
220630-441-GP	30/06/22	340	29.2	150	3:45	1	30.2	45.4		90	23.0	33.1		2.2	0.59	2.3
220629-439-GP	29/06/22	320	29.3	135	3:45	1	28.9	43.9						2.2	0.58	2.1
220626-136-GP	26/06/22	335	30.0	150	4:30	1	29.1	41.8		100	20.1	31.9		2.3	0.57	2.2
220617-574-GP	17/06/22	325	29.0	120	4:00	1	30.0	43.5	64.9					2.4	0.57	2.2
220612-570-GP	12/06/22	355	30.4	150	4:00	1	31.2	44.6	65.3	90	23.5	33.4	49.9	2.3	0.56	2.2
220606-259-GP	06/06/22	335	29.3	150	4:15	1	29.4	42.4	63.8					2.0	0.58	2.3
220604-257-GP	04/06/22	335	29.3	150	4:00	1	28.8	41.7	65.8	100	22.6	32.7	48.3	1.8	0.55	2.2
220602-135-GP	02/06/22	320	29.4	150	3:45	2	30.1	43.6	64.9					2.2	0.56	2.2
220530-907-GP	30/05/22	330	29.4	150	3:45	1	32.2	46.3	65.1	100	24.1	33.0	47.0	2.1	0.57	2.2
220527-492-GP	27/05/22	320	29.4	150	4:15	1	31.4	44.1	66.5					2.3	0.57	2.2
220522-489-GP	22/05/22	325	29.4	135	4:00	2	31.8	43.8	65.8	110	20.9	32.3	44.8	2.0	0.58	2.2
220520-114-GP	20/05/22	345	29.5	150	4:15	1	31.6	44.8	65.8					2.0	0.57	2.2
220518-112-GP	18/05/22	340	29.5	150	4:15	2	30.5	43.4	65.7	80	24.0	34.0	47.5	2.2	0.56	2.2
220512-768-GP	12/05/22	340	29.1	135	3:30	2	30.9	41.9	64.6	70	23.3	35.4	47.4	1.9	0.54	2.2
220509-771-GP	09/05/22	340	29.0	150	3:45	1	29.1	41.5	64.1					1.7	0.57	2.3
220503-431-GP	03/05/22	345	29.1	135	3:30	1	30.5	42.0	63.6	100	22.9	32.5	45.6	2.3	0.56	2.3
220501-433-GP	01/05/22	340	28.6	135	3:45	1	29.7	39.6	62.7					2.8	0.56	2.3
220428-081-GP	28/04/22	355	28.7	135	3:45	2	30.7	42.6	64.6					2.2	0.58	2.3
220425-079-GP	25/04/22	350	28.6	135	3:45	1	30.0	41.4	62.7	90	23.5	32.2	46.1	2.3	0.57	2.2
220420-977-GP	20/04/22	365	28.8	165	4:15	1	31.1	43.1	63.0					2.0	0.56	2.2
220416-828-GP	16/04/22	360	28.8	165	4:00	1	30.6	42.2	62.4	100	20.2	30.3	42.5	1.9	0.56	2.2

The above samples were tested as received in accordance with the current terms of accreditation and methods stated in NZS 3122:2009 with the exception of:

Chemical composition to ASTM C114-18

- Concrete Compressive Strength test results outside the scope of accreditation

# No result available at time of certificate issue

This Report must not be reproduced except in full

Raki Harding  
Quality Manager

Date issued: 22/07/2022




Portland Works, Portland, Whangarei 0178



**EverSure™  
Type GP Cement**



**Compressive Strength ISO-CEN Mortar  
(Bulk Dispatch)**

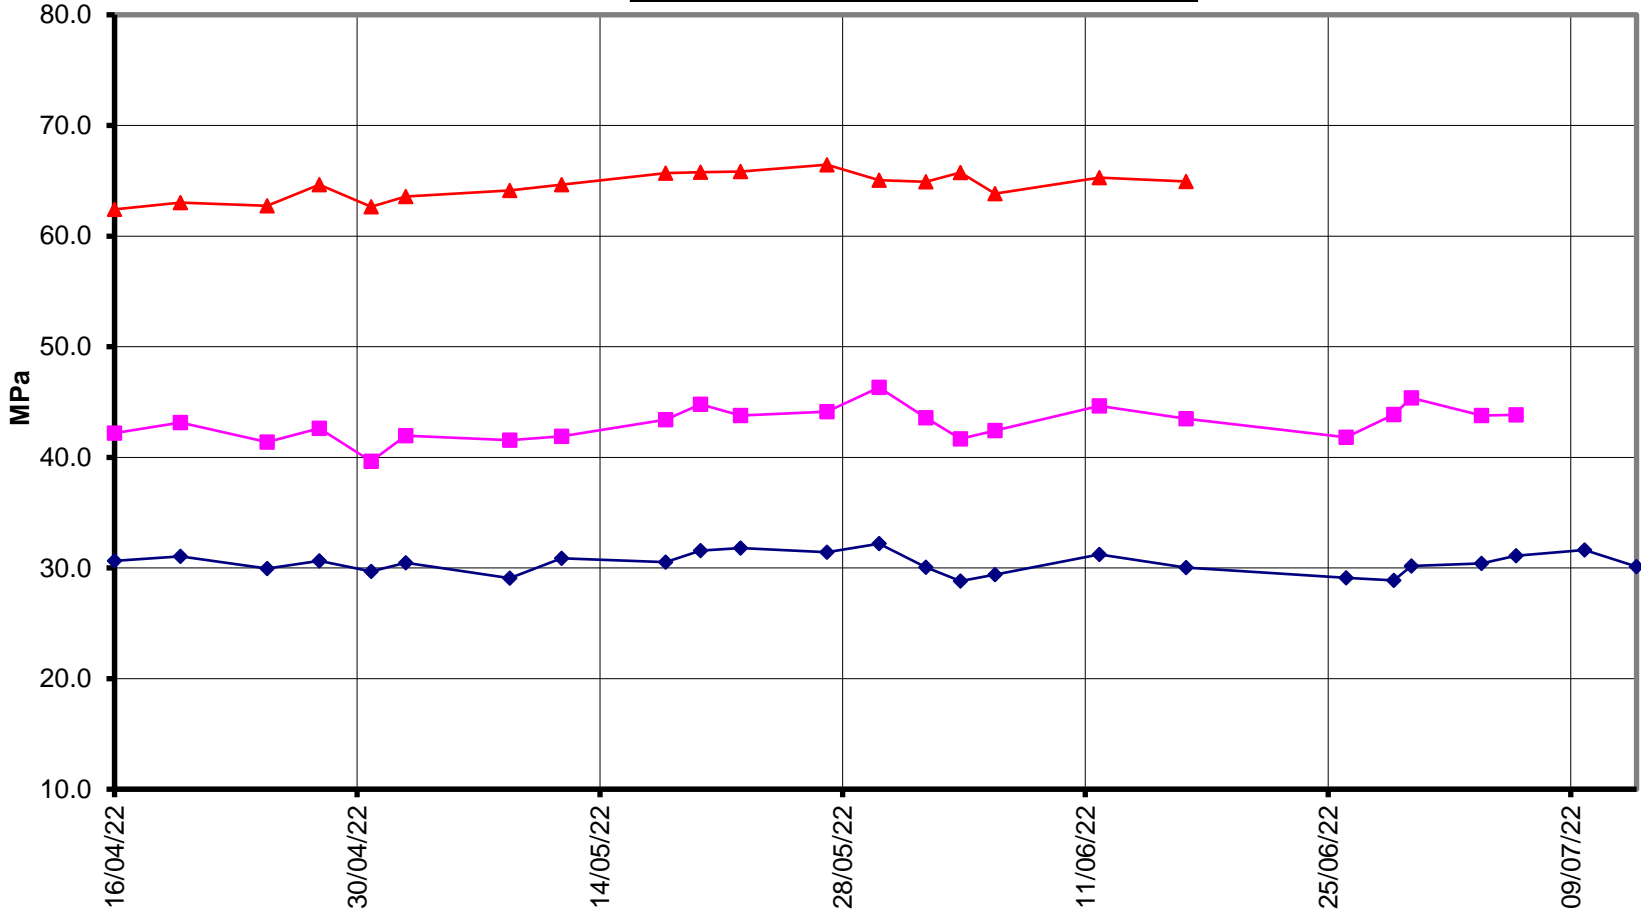

Date





# EverSure™ Type GP Cement



## Compressive Strength Concrete (Bulk Dispatch)

—x— 28 Days    —■— 7 Days    —◆— 3 Days    —x— Slump

