



CERTIFICATE OF QUALITY

EcoSure® Type GP Cement

NZS3122:2009 (Bulk & Bag Despatch)



Issued to: National Sales Manager

Test Report No: 23#56

info@goldenbay.co.nz

Code	Week Ending / Voyage	Specific Surface Area	Normal Consistency	Initial Set	Final Set	Soundness	Compressive Strength						Free Lime	Sodium Equivalent (NaEq)	Sulphur Trioxide (SO3)	
							ISOCEN			Concrete						
							3 days	7 days	28 days	Slump	3 days	7 days				28 days
Mean		343	29.1	149	3:52	1	32.5	45.8	65.0	97	22.8	33.7	45.7	1.4	0.57	2.1
Standard Deviation		8	0.2	9	0:10	0	0.9	1.3	1.3	6	1.2	2.3	3.3	0.1	0.01	0.02
Min		330	28.8	135	3:30	0	30.4	43.3	63.0	90	21.4	31.4	38.9	1.1	0.54	2.1
Max		360	29.9	165	4:15	2	34.3	48.6	67.5	105	25.2	38.0	51.8	1.7	0.59	2.2
NZS 3122:2009 Requirements				45 min	6:00 max	5 max		35.0 min	45.0 min						0.6 max	3.5 max
Units		m2/kg	%	minutes	hrs:mins	mm	MPa	MPa	MPa	mm	MPa	MPa	MPa	%	%	%
230519-741-GP	19/05/23	340	29.0	165	4:15	1	31.4							1.6	0.56	2.2
230512-679-GP	12/05/23	350	29.9	165	4:00	1	32.3							1.7	0.55	2.2
230510-509-GP	10/05/23	330	29.6	150	4:15	2	30.4	43.3						1.5	0.54	2.1
230506-507-GP	06/05/23	335	29.3	150	4:00	1	32.3	45.8						1.4	0.55	2.1
230502-178-GP	02/05/23	330	29.2	135	4:00	0	32.4	47.7						1.4	0.55	2.1
230427-851-GP	27/04/23	350	28.8	135	3:45	1	32.4	47.2						1.4	0.57	2.2
230425-853-GP	25/04/23	350	29.2	135	3:45	1	32.6	46.3						1.5	0.55	2.1
230421-495-GP	21/04/23	345	28.9	135	3:45	0	32.1	45.4	65.2	105	22.8	32.2	38.9	1.5	0.59	2.1
230420-497-GP	20/04/23	345	29.0	150	4:00	1	31.4	43.4	63.0					1.4	0.56	2.1
230414-218-GP	14/04/23	350	29.2	150	3:45	1	32.4	44.2	65.1					1.5	0.57	2.2
230410-216-GP	10/04/23	330	29.1	150	3:45	1	33.1	46.1	66.9	90	24.1	31.4	46.1	1.6	0.57	2.2
230405-145-GP	05/04/23	345	29.0	150	4:00	1	32.2	45.1	64.0					1.1	0.58	2.2
230402-980-GP	02/04/23	355	29.0	150	4:00	1	33.3	47.0	63.8	100	21.4	33.6	44.8	1.3	0.58	2.2
230331-831-GP	31/03/23	345	29.2	150	4:00	2	31.3	43.8	63.1					1.4	0.58	2.1
230328-653-GP	28/03/23	345	29.2	150	4:00	1	31.9	44.9	64.4	90	25.2	38.0	47.2	1.3	0.57	2.1
230323-331-GP	23/03/23	330	29.0	150	4:00	1	33.2	45.7	65.1	105	22.6	31.8	46.8	1.3	0.57	2.2
230318-091-GP	18/03/23	340	29.0	150	3:45	1	33.4	46.8	65.3					1.3	0.57	2.1
230314-089-GP	14/03/23	355	29.0	150	3:45	1	33.7	45.1	64.2	100	22.8	33.1	46.2	1.4	0.55	2.2
230311-659-GP	11/03/23	350	28.8	135	3:30	1	34.3	48.6	67.5					1.1	0.57	2.2
230309-657-GP	09/03/23	340	28.9	150	3:45	2	33.4	46.4	65.3	90	23.9	37.7	51.8	1.5	0.55	2.2
230301-330-GP	01/03/23	335	28.9	150	3:45	1	33.9	47.2	67.0					1.3	0.58	2.1
230225-291-GP	25/02/23	345	28.8	150	3:45	1	32.5	45.9	65.7	100	21.8	33.1	43.6	1.4	0.58	2.1
230223-005-GP	23/02/23	340	29.1	150	3:45	1	32.3	45.4	63.7					1.5	0.58	2.2
230221-003-GP	21/02/23	345	28.9	165	3:45	1	32.5	46.3	64.6	100	21.5	33.3	43.8	1.4	0.58	2.2
230216-805-GP	16/02/23	360	28.9	150	3:45	1	31.5	45.2	65.2	90	22.3	32.7	47.4	1.4	0.57	2.1

The above samples were tested as received in accordance with the current terms of accreditation and methods stated in NZS 3122:2009 with the exception of:

Chemical composition to ASTM C114-18

All concrete testing conducted in accordance with NZS 3112:1986.

Sample Retested

This Report must not be reproduced except in full

Vincent Lane
Works Chemist



Portland Works, Portland, Whangarei 0178

Date issued: 26/05/2023

Page 1 of 3




EcoSure® Type GP Cement

Compressive Strength ISO-CEN Mortar (Bulk Dispatch)



28 Days 7 Days 3 Days

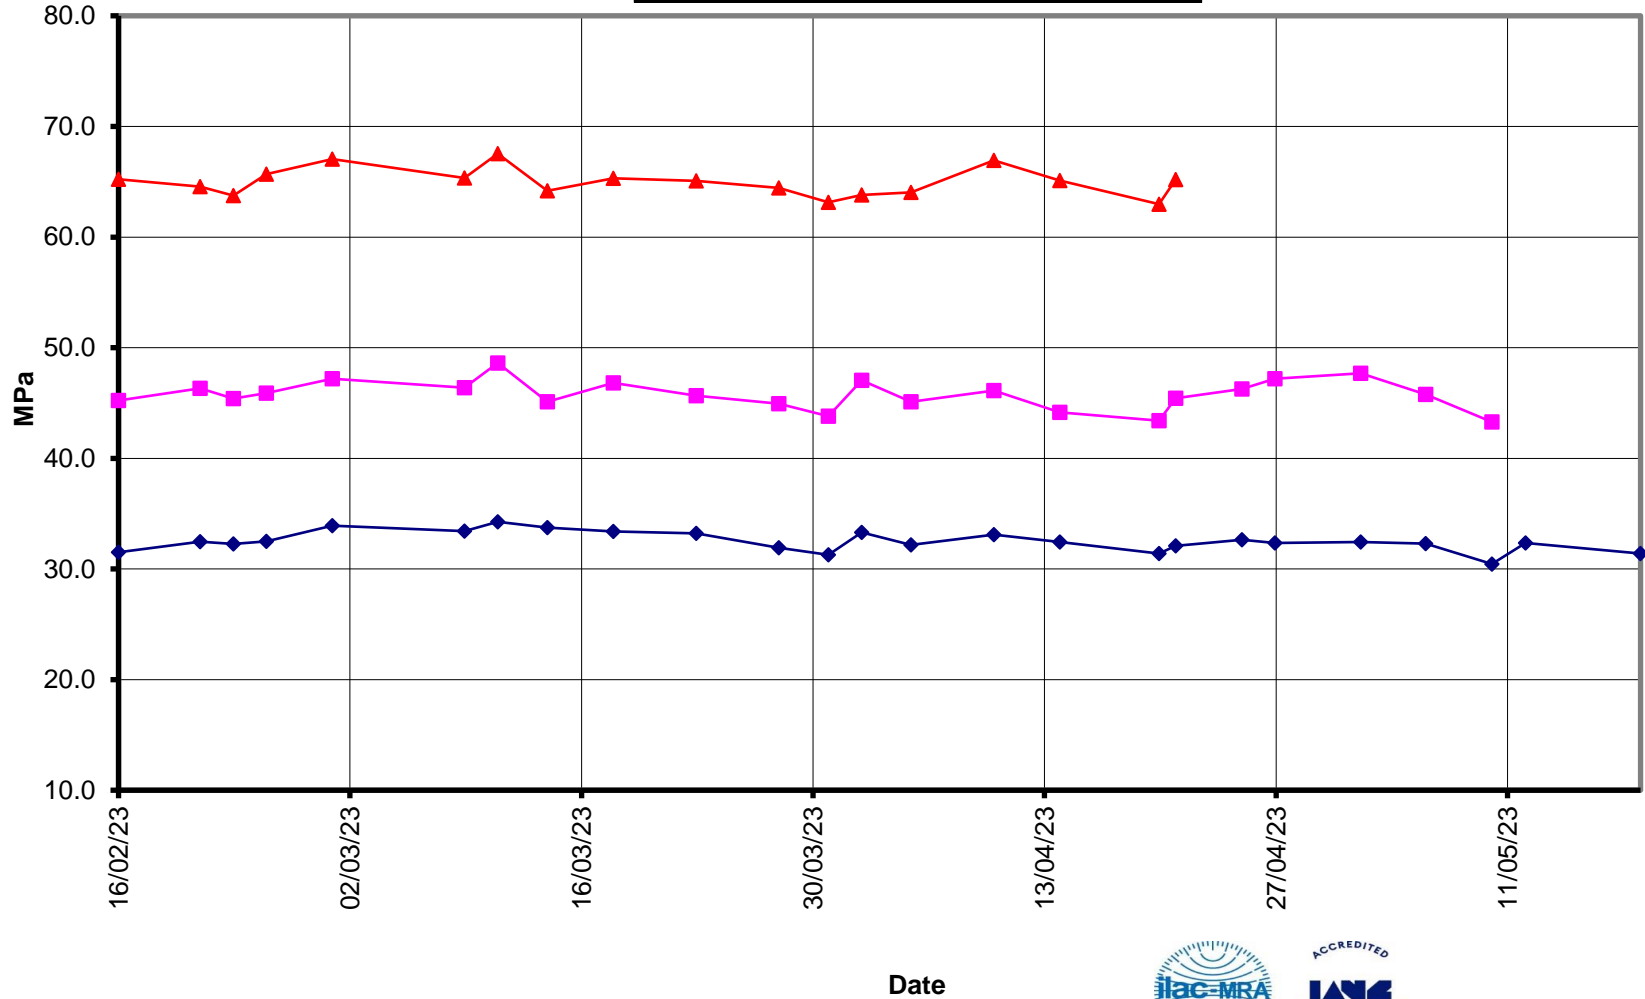



EcoSure® Type GP Cement

Compressive Strength Concrete (Bulk Dispatch)



—x— 28 Days —■— 7 Days —◆— 3 Days —x— Slump

