



# CERTIFICATE OF QUALITY

## EverSure™ Type GP Cement

NZS3122:2009 (Bulk Despatch)



Our  
NZ made  
cement is  
genuine  
NZ grade  
cement.

Issued to: National Sales Manager

Test Report No: 20#06

info@goldenbay.co.nz

Code	Week Ending / Voyage	Specific Surface Area	Normal Consistency	Initial Set	Final Set	Soundness	Compressive Strength						Free Lime	Sodium Equivalent (NaEq)	Sulphur Trioxide (SO3)	
							ISOCEN			Concrete						
							3 days	7 days	28 days	Slump	3 days	7 days				28 days
Mean		330	28.7	136	3:31	1	32.9	45.5	65.6	93.1	25.7	35.1	46.6	2.0	0.53	2.2
Standard Deviation		9	0.1	8	0:09	0.4	1.2	1.3	1.4	4.8	2.2	2.0	1.8	0.2	0.01	0.0
Min		315	28.7	120	3:15	0	30.6	43.1	63.3	90.0	23.1	32.4	43.6	1.3	0.51	2.2
Max		355	28.9	150	3:45	2	35.5	48.3	67.6	100.0	30.9	37.2	49.9	2.3	0.55	2.3
NZS 3122:2009 Requirements				45 max	6:00 max	5 max		35.0 min	45.0 min						0.6 max	3.5 max
Units		m2/kg	%	minutes	hrs:mins	mm	MPa	MPa	MPa	mm	MPa	MPa	MPa	%	%	%
200103-087-GP	01/01/20	320	28.9	120	3:30	1	32.4			90	25.9			1.8	0.54	2.2
191227-420-GP	27/12/19	325	28.9	135	3:30	1	30.8	46.4						1.9	0.53	2.2
191223-407-GP	23/12/19	320	28.8	135	3:30	1	30.7	43.1		90	25.2			1.8	0.53	2.2
191219-013-GP	19/12/19	340	28.8	135	3:15	1	30.6	47.0		100	23.1			2.0	0.52	2.2
191215-016-GP	15/12/19	325	28.8	120	3:15	1	31.8	45.6						1.3	0.55	2.2
191213-602-GP	13/12/19	325	28.7	135	3:30	1	32.5	44.9		90	25.8	36.3		2.0	0.55	2.2
191211-600-GP	11/12/19	330	28.7	135	3:30	1	31.6	45.0						2.1	0.54	2.2
191207-225-GP	07/12/19	335	28.7	120	3:15	1	32.2	43.7	63.8					1.8	0.55	2.3
191204-223-GP	04/12/19	340	28.7	135	3:15	1	33.4	44.7	64.6	90	28.3	37.0	49.9	2.0	0.54	2.2
191129-877-GP	29/11/19	335	28.7	135	3:30	1	33.6	45.8						2.0	0.52	2.2
191128-830-GP	25/11/19	330	28.7	135	3:45	2	33.5	46.6	63.9	90	24.4	32.8	47.0	2.3	0.53	2.2
191122-545-GP	22/11/19	355	28.7	135	3:45	2	35.5	48.3	67.6					2.0	0.53	2.2
191120-479-GP	20/11/19	330	28.7	135	3:30	1	33.8	46.6	65.8	100	23.5	32.4	44.7	2.2	0.54	2.2
191115-183-GP	15/11/19	330	28.7	135	3:30	1	33.8	45.7	64.5	100	25.2	34.7	43.6	2.0	0.52	2.2
191112-181-GP	12/11/19	325	28.8	135	3:30	1	32.9	45.2	65.5					2.1	0.54	2.2
191106-750-GP	06/11/19	335	28.8	150	3:30	1	34.0	46.4	67.2	90	30.9	37.2	45.7	2.1	0.53	2.2
191103-752-GP	03/11/19	335	28.8	150	3:45	2	33.1	43.8	65.1					2.3	0.53	2.2
191101-352-GP	01/11/19	330	28.7	150	3:30	1	33.7	44.6	64.7	90	28.1	37.1	47.3	2.3	0.54	2.2
191030-354-GP	30/10/19	340	28.7	135	3:30	2	33.3	45.7	66.1					2.0	0.53	2.2
191028-981-GP	28/10/19	320	28.7	150	3:30	1	33.5	46.3	65.3					2.3	0.53	2.2
191024-979-GP	24/10/19	325	28.7	135	3:30	0	33.1	44.8	67.4	90	25.4	36.9	47.4	2.3	0.53	2.2
191017-569-GP	17/10/19	315	28.8	135	3:45	1	33.6	43.4	65.2	90	25.4	33.2	47.1	2.0	0.52	2.2
191013-571-GP	13/10/19	330	28.7	135	3:45	1	33.0	46.9	63.3					2.1	0.52	2.2
191010-383-GP	10/10/19	320	28.8	135	3:45	1	33.5	45.4	67.4					1.9	0.51	2.2
191007-381-GP	07/10/19	330	28.8	135	3:30	1	33.9	46.7	66.9	100	23.4	33.0	46.9	2.0	0.51	2.2

This Report must not be reproduced except in full

The above samples were tested as received in accordance with the current terms of accreditation and methods stated in NZS 3122:2009 with the exception of:

Chemical composition to ASTM C114-18

- Concrete Compressive Strength test results outside the scope of accreditation



Portland Works, Portland, Whangarei 0178

Sample retested  
# No result available at time of certificate issue

Jim White  
Quality System Co-ordinator

Date issued: 10/01/2020

Page 1 of 3




**EverSure™  
Type GP Cement**



**Compressive Strength ISO-CEN Mortar  
(Bulk Despatch)**

—x— 28 Days    —■— 7 Days    —◆— 3 Days

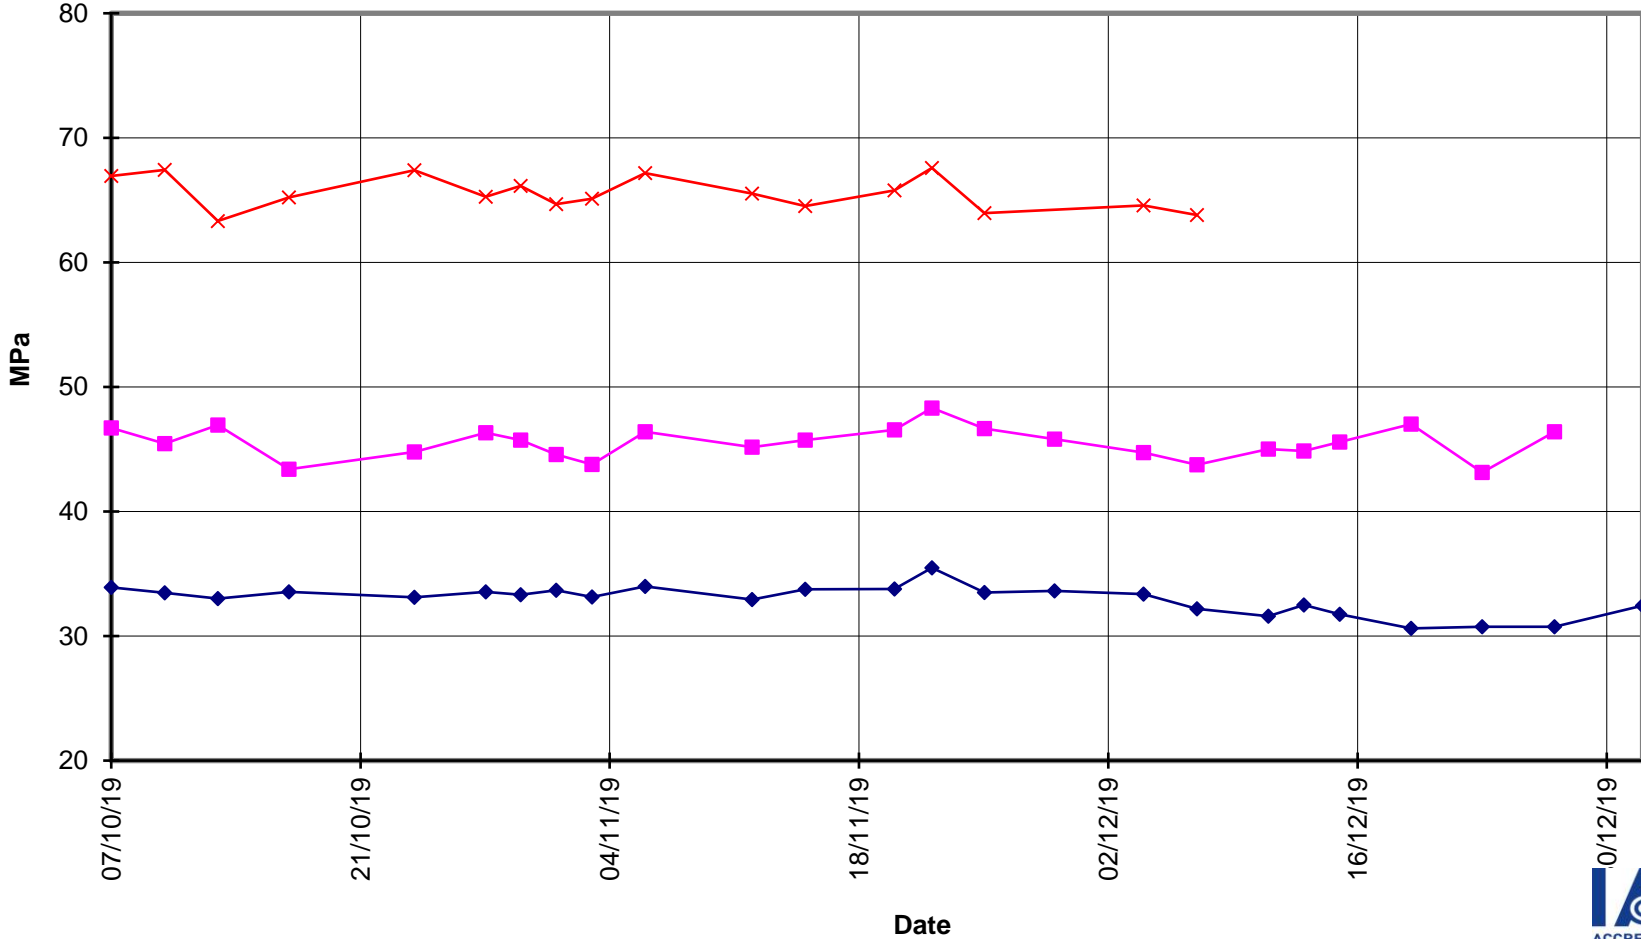



**EverSure™  
Type GP Cement**



**Compressive Strength Concrete  
(Bulk Despatch)**

—x— 28 Days —■— 7 Days —◆— 3 Days —■— Slump

